

# Monthly Performance Report – July 2022

---

RAIL SAFETY DIVISION

August 23, 2022



**California Public  
Utilities Commission**


# Table of Contents

|  |    |
|--|----|
| COMPLIANCE WITH ORDERING PARAGRAPHS.....                               | 1  |
| MONITORING THE WHISTLEBLOWER WEBSITE.....                              | 2  |
| Statistics – 1/1/22 – 7/31/22 .....                                    | 2  |
| RAILROAD OPERATIONS AND SAFETY BRANCH - ROSB.....                      | 3  |
| ROSB Inspection, Investigation & Field Activities .....                | 3  |
| Crude Oil Reconnaissance Team (CORT) Monthly Report.....               | 7  |
| RAIL CROSSINGS AND ENGINEERING BRANCH - RCEB .....                     | 10 |
| Rail Crossing Incident Investigations .....                            | 10 |
| Safety Assesments, Quiet Zones and Reviews .....                       | 11 |
| Proceedings, Resolutions and G.O. 88B Reviews .....                    | 12 |
| RAIL TRANSIT SAFETY BRANCH - RTSB .....                                | 13 |
| Major Audits .....   | 13 |
| Administrative Accomplishments .....                                   | 13 |
| General Order and Resolution Activity .....                            | 14 |
| RTA Ongoing Projects .....   | 14 |
| Bay Area Rapid Transit - BART.....                                     | 14 |
| Los Angeles County Metropolitan Transportation Authority - LACMTA..... | 16 |
| Los Angeles World Airports - LAWA.....                                 | 19 |
| Orange County Transportation Authority - OCTA.....                     | 20 |
| Sacramento Regional Transit District - SRTD.....                       | 20 |
| San Diego Metropolitan Transit System - SDMTS.....                     | 21 |
| Santa Clara Valley Transportation Authority - SCVTA.....               | 21 |
| San Francisco Municipal Transportation Authority - SFMTA.....          | 23 |
| Appendices.....  | 24 |
| Corrective Actions Plans.....  | 24 |
| Accident Investigations.....   | 24 |
| Monthly RTSB Data/Statistics Summary.....                              | 25 |
| Ongoing Data/Trends.....   | 26 |



## Compliance with Ordering Paragraphs (COPS)

Through July 31, 2022, the Rail Safety Division (RSD) showed 529 total entries in the COPS system, with 28 (5%) reaching compliance, 490 (93%) not yet due for compliance, and 11 (2%) out of compliance. 529 (100%) of all Ordering Paragraphs (OP) are assigned to RSD staff.

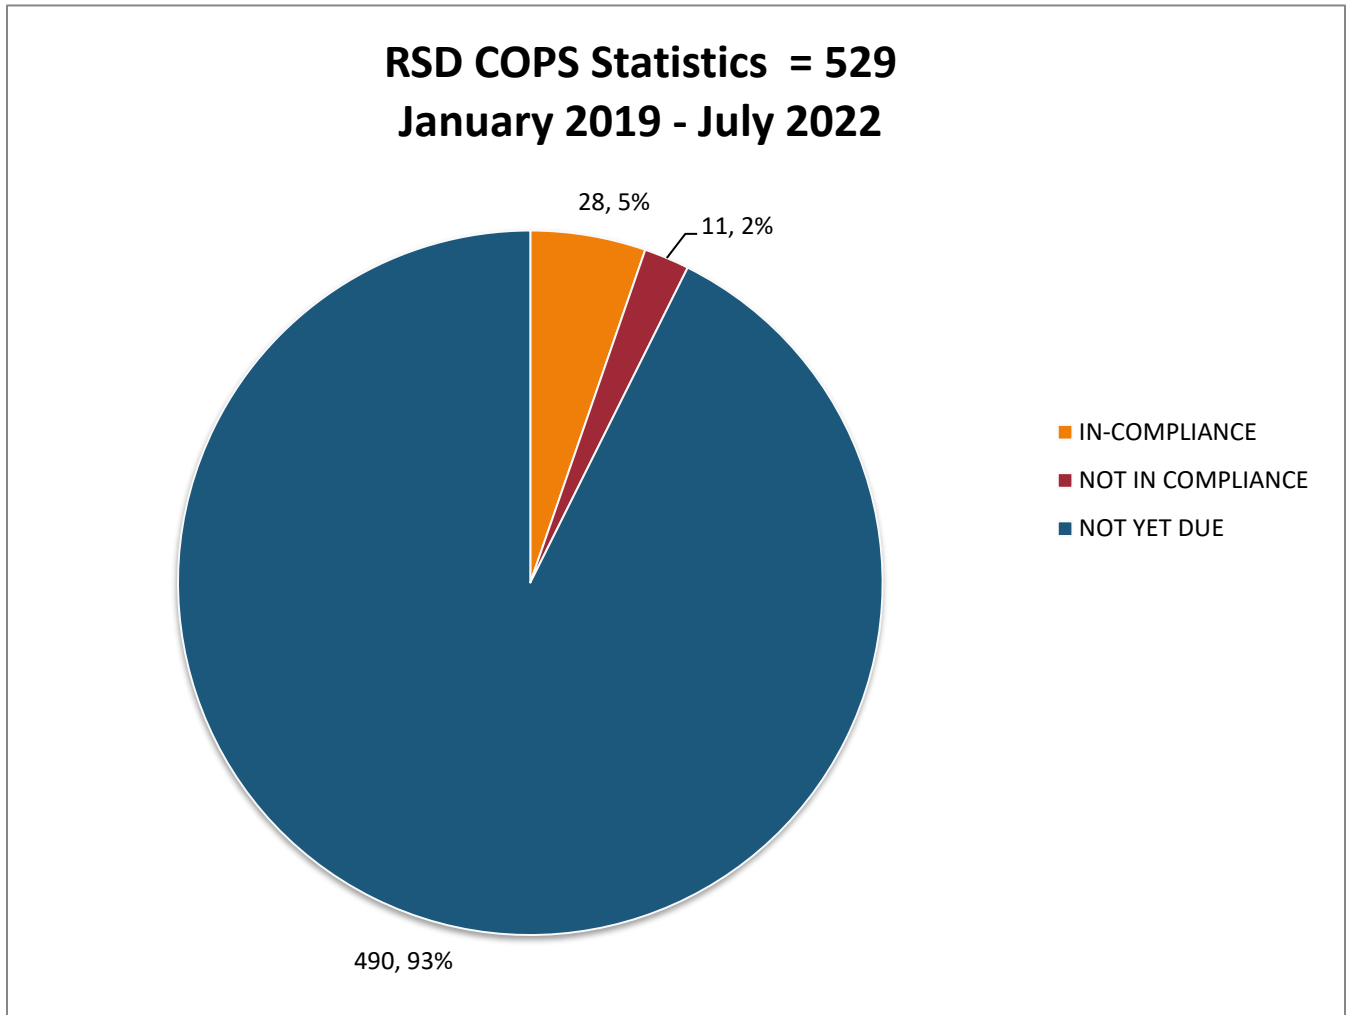

## Monitoring the Whistleblower Website

---

The Risk Section has been overseeing intake for complaints that arrive via a “whistleblower” application on the Commission’s web site. Whistleblower protections are afforded to utility employees and contractors who report potentially unsafe or illegal practices.

### Statistics – 1/1/2022 – 7/31/2022

---

Note: This is for complaints filed using the on-line Whistleblower Application ONLY.



## Railroad Operations and Safety Branch - ROSB

---

In July 2022, the RSD Railroad Operations and Safety Branch (ROSB) completed the following:

| <b>Railroad Operations and Safety Branch</b>         | <b>July-2022</b> | <b>YTD 2022</b> |
|--|------------------|-----------------|
| <b>New Incidents Investigated</b>                    | 8                | 45              |
| <b>Informal Complaints Investigated</b>              | 1                | 15              |
| <b>Railroad Bridge Observations</b>                  | 8                | 84              |
| <b>Railroad Safety Inspections</b>                   | 253              | 1787            |
| <b>Non-compliant conditions identified/corrected</b> | 584              | 4862            |
| <b>Operation Lifesaver Presentations</b>             | 35               | 44              |

### ROSB Inspection, Investigation & Field Activities

---

**July 7, 2022:** RSD Railroad Safety Inspectors performed an inspection of the Union Pacific (UP) West Colton yard in Bloomington. During the inspection, inspectors observed a rail car containing a load of Acetic Acid, a hazardous material, with a closure that was not properly secured.

Title 49 Code of Federal Regulations (CFR) 173.31.(d) (1) (iv) states shippers must verify all closures and fastenings on tank cars are properly secured and tightened in place by use of a bar, wrench, or other suitable tool. Securing all closures is essential to assure that the product will not be released during transit, placing the public at risk for exposure. The UP manager was notified of the unsafe condition who took remedial action to correct the condition and bring it into regulatory compliance which was verified by the inspector.

**July 11, 2022:** RSD Railroad Safety Inspectors performed a General Order (GO) inspection on the California Northern Railroad (CFNR) in Woodland. The following non-compliant condition was observed:


The inspectors observed multiple piles of tree trimmings left in the walkway on the east side of the main track which created tripping hazards for railroad employees working in the area. This is not in compliance with GO 118-A, which provides standards for the construction, reconstruction, and maintenance of walkways adjacent to railroad tracks to provide a safe area for railroad employees to work.



This non-compliant condition was brought to the attention of the CFNR manager who stated that he would have the piles removed. A follow-up inspection was conducted on July 21<sup>st</sup> and the inspector verified that the tree trimmings had been removed.

**July 27, 2022:** An RSD Rail Safety Inspector performed an inspection at the UP intermodal rail terminal in the City of Industry to verify compliance of railroad freight equipment. The inspector examined railroad freight equipment that was deemed ready for transportation by TTX, a contractor company that performs repairs on freight railroad cars.



Upon inspection of the equipment, several non-compliant conditions were discovered, which included two broken snubber activating springs on the same freight car in different locations. Also identified was a freight car with brakes not in effective operating condition because the brake did not apply firmly onto the wheel therefore no brakes were applied to the wheels of the freight car.


The inspector identified six non-compliant conditions and recommended two civil penalties. The inspector immediately notified UP management of the non-compliant conditions and issued an inspection report. UP made corrective repairs to the non-complying equipment prior to the train’s departure from the terminal as was verified by the inspector.

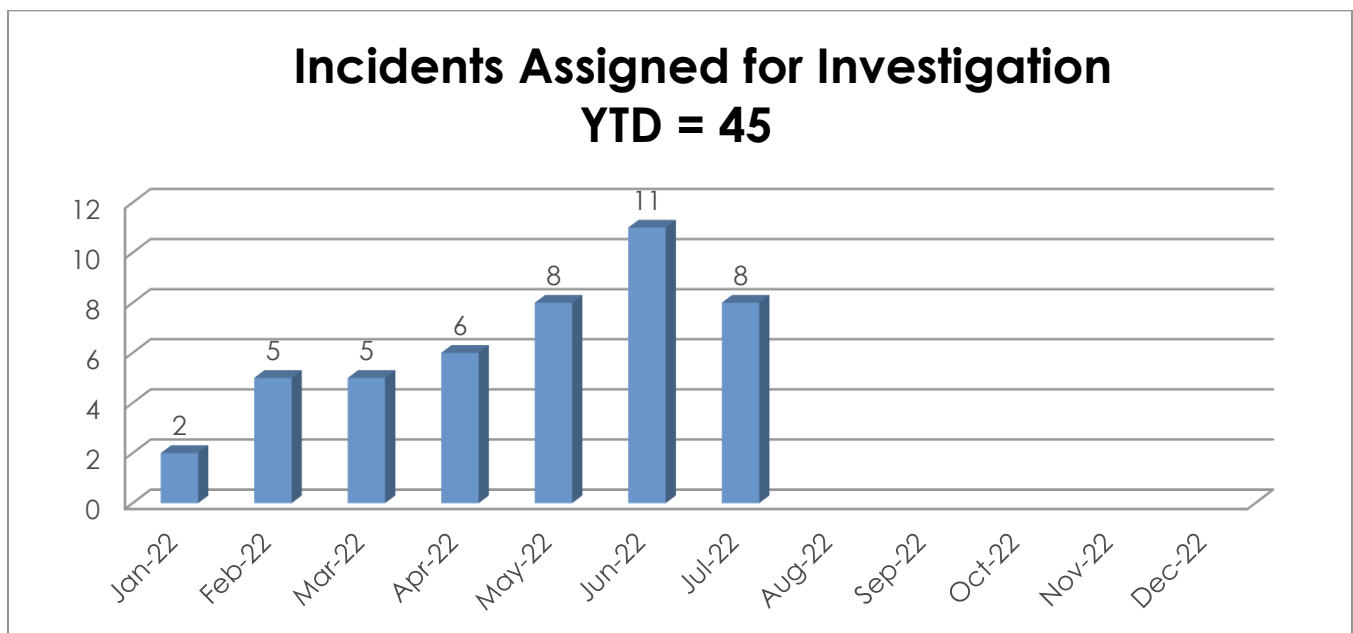

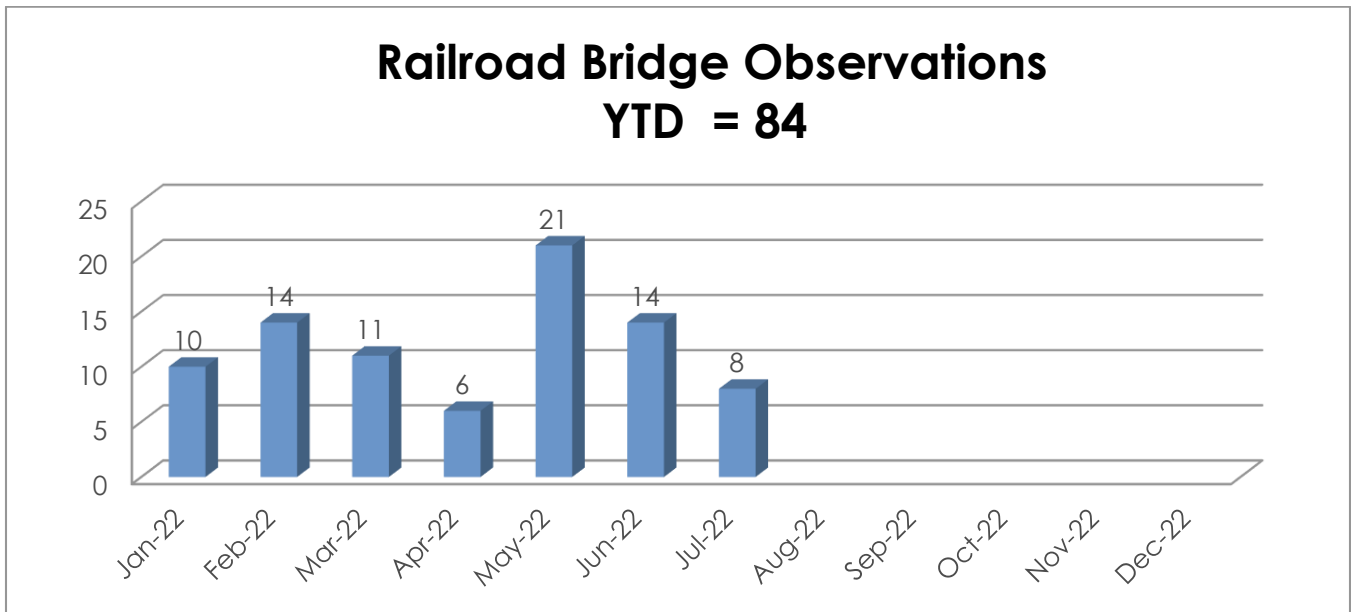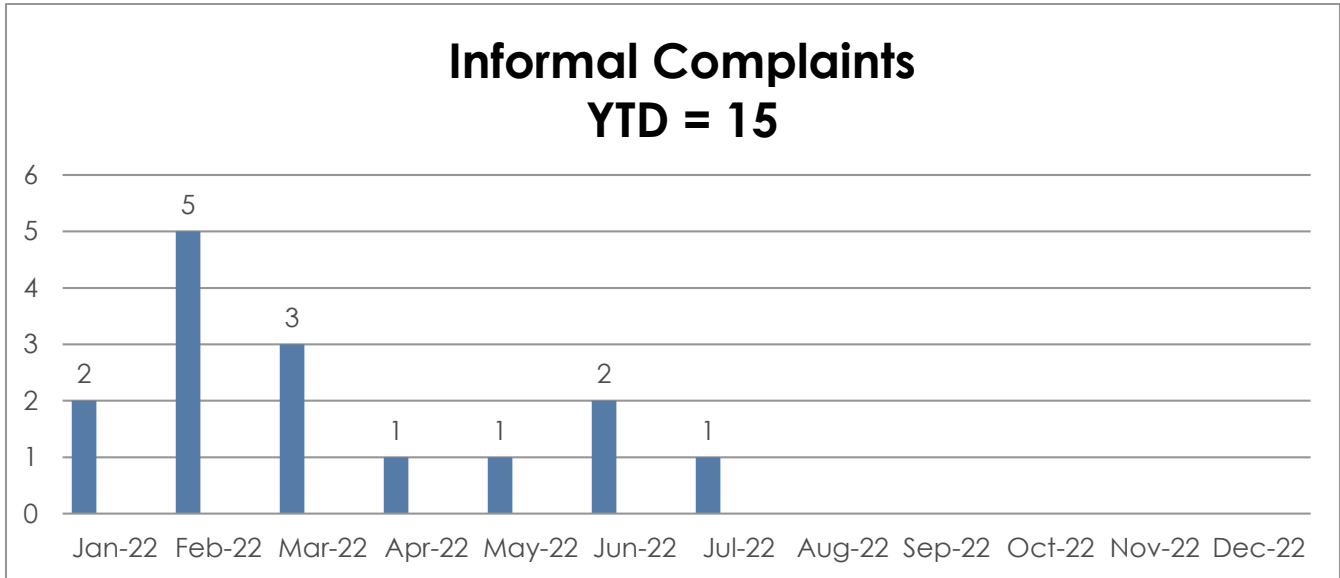



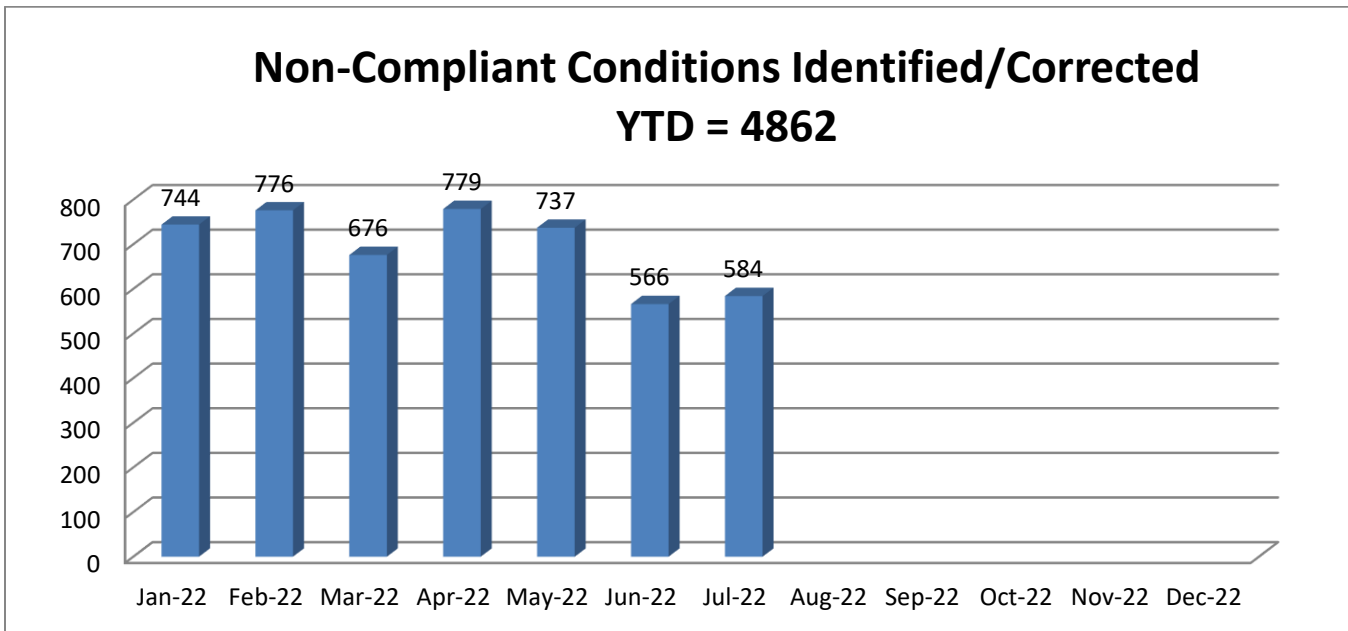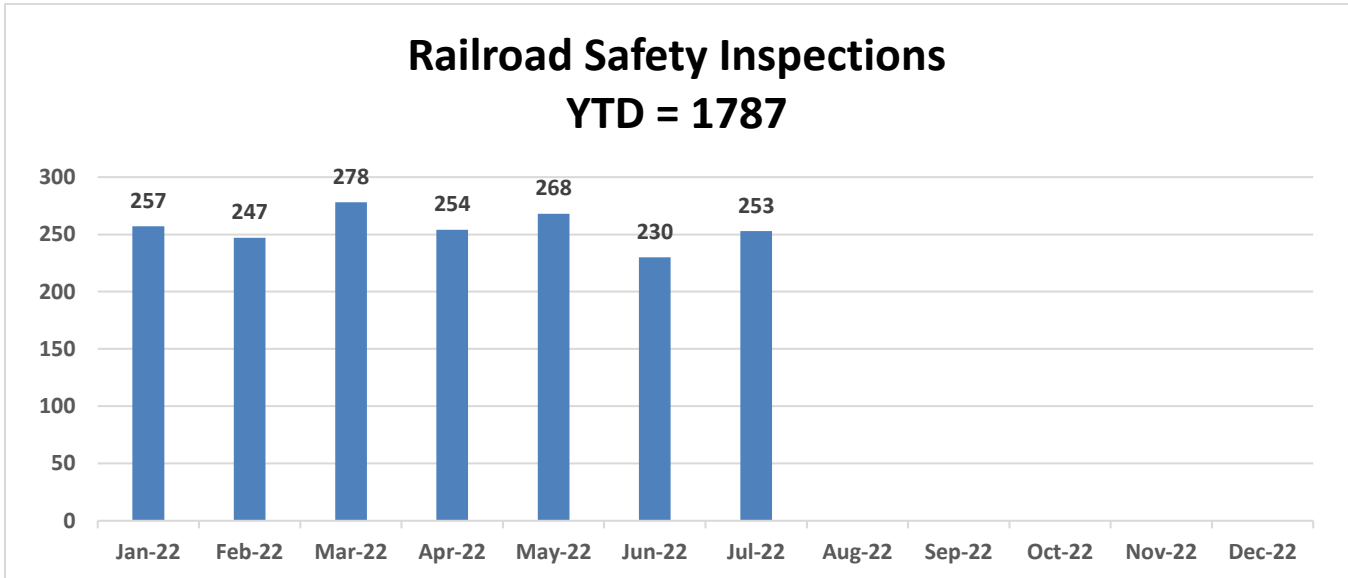

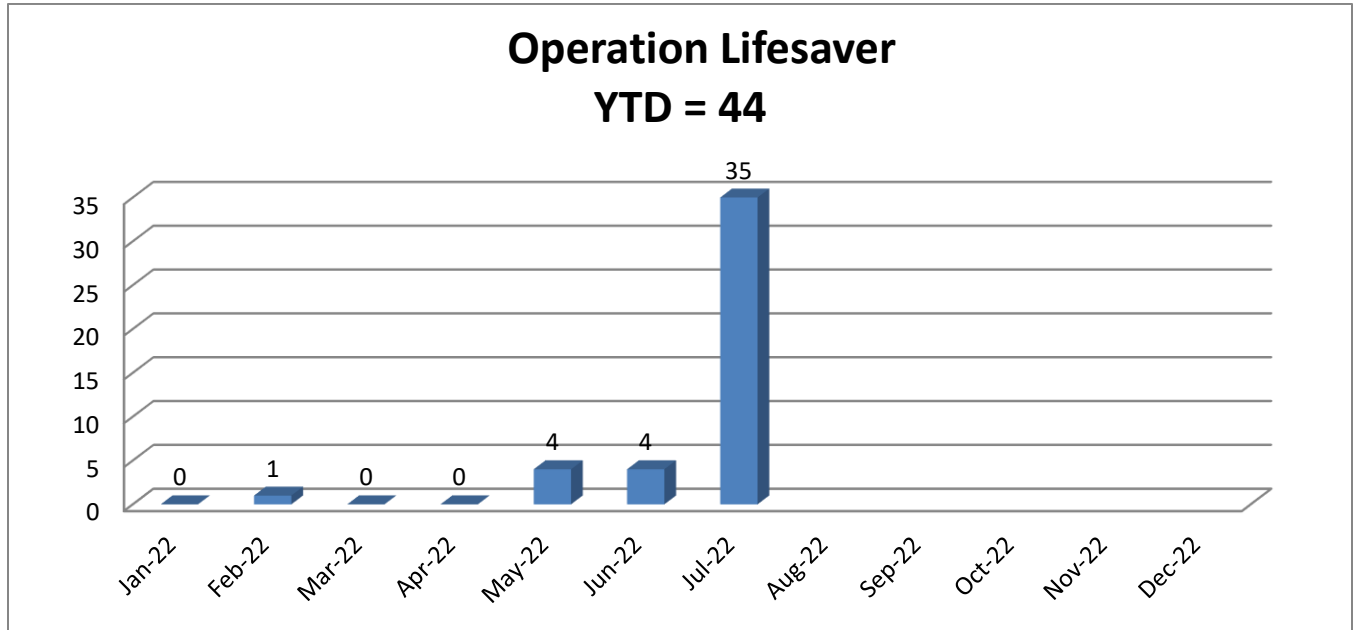

### Crude Oil Reconnaissance Team (CORT) Monthly Report

The CORT was formed in 2014 in response to highly volatile crude oil transportation in North America. The CORT’s purpose is to monitor crude oil transported by rail into California. This report tracks CORT activities, crude oil unit trains<sup>1</sup> entering California each month and the type of crude oil being transported.

The CORT’s role was expanded in 2018 to include tracking ethanol unit trains entering the state and documenting the location of stored hazardous material tank cars.

| Crude Oil Shipments in California |                       |                             |                                |                            |                      |                         |                     |
|-----------------------------------|-----------------------|-----------------------------|--------------------------------|----------------------------|----------------------|-------------------------|---------------------|
| Consignee <sup>2</sup>            | Highly Volatile (Y/N) | # Unit Trains Received July | # Unit Trains Projected August | # Unit Trains FYTD (22-23) | # Cars Received July | # Cars Projected August | # Cars FYTD (22-23) |
| Plains All America                | N                     | 0                           | 0                              | 0                          | 0                    | 0                       | 0                   |

<sup>1</sup> A unit train is a freight train composed of cars carrying a single type of commodity that are all bound for the same destination.

<sup>2</sup> See Appendix A for descriptions of Consignees and Railroads.

| Kern Oil                                   | N                           | 1                              | 1                          | 1                    | 100                     | 100                 | 100 |
|--|-----------------------------|--------------------------------|----------------------------|----------------------|-------------------------|---------------------|-----|
| Ethanol Unit Train Shipments in California |                             |                                |                            |                      |                         |                     |     |
| Consignee                                  | # Unit Trains Received July | # Unit Trains Projected August | # Unit Trains FYTD (22-23) | # Cars Received July | # Cars Projected August | # Cars FYTD (22-23) |     |
| Kinder Morgan (Wilmington)                 | 18                          | 17                             | 17                         | 1723                 | 1700                    | 1723                |     |
| Eco-Energy (Stockton)                      | 0                           | 3                              | 0                          | 0                    | 300                     | 0                   |     |
| Pelican Renewables (Stockton)              | 3                           | 1                              | 3                          | 324                  | 100                     | 324                 |     |
| Storage of Hazardous Material Cars         |                             |                                |                            |                      |                         |                     |     |
| Railroad                                   | Loads                       | Empties                        | Commodity                  | County               |                         |                     |     |
| Arizona California RR                      | 79                          | 164                            | LPG                        | San Bernardino       |                         |                     |     |
| SMART                                      | 0                           | 0                              | LPG                        | Marin                |                         |                     |     |
| Santa Maria RR                             | 3                           | 174                            | LPG                        | Santa Barbara        |                         |                     |     |
| Sierra Northern Railway                    | 333                         | 147                            | LPG                        | Stanislaus           |                         |                     |     |
| Oakland Global Rail Enterprise             | 10                          | 137                            | LPG                        | Alameda              |                         |                     |     |
| Yreka Western RR                           | 0                           | 0                              | N/A                        | Siskiyou             |                         |                     |     |

### Appendix A

#### Crude Oil Consignees

**Delta Trading** in Bakersfield has oil cars delivered by manifest train. Delta is still seeking a new customer.

**Kern Oil** in Bakersfield has unit trains delivered by the San Joaquin Valley Railroad (SJVR).

**Plains All America** in Taft has unit trains delivered by the SJVR.

### **Ethanol Unit Train Consignees**

**Kinder Morgan** is a pipeline and off-loading facility located in Wilmington, that receives 64 or 96 car unit trains delivered by the BNSF.

**Eco-Energy** is an energy provider in Stockton, that receives 100 to 112 car ethanol unit trains delivered by the Central California Traction Company.

**Pelican Renewables** is an energy provider in Stockton, that receives 96 to 108 car ethanol unit trains delivered by the Central California Traction Company.

### **Hazardous Material Car Storage Locations**

**Arizona-California Railroad** is a short line railroad that operates over 91 miles between Cadiz and Parker, Arizona. A spur track located in Rice, owned by the railroad but leased by PBF Energy for the storage of tank cars. Cars are Interchanged at Cadiz with BNSF.

**Northwestern Pacific Railroad** is a regional railroad that currently operates 62 miles of track between Schellville and Windsor and interchanges with the Union Pacific Railroad.

**Santa Maria Railroad** is a short line railroad that operates over 14 miles of track and interchanges with the UPRR in Guadalupe.

**Sierra Northern Railway** is a short line railroad that operates over 100 miles of track in Mendocino, Tuolumne, Stanislaus, and Yolo counties. Sierra Northern provides rail shipping to all of California through interchanges with the BNSF and UPRR.

**Oakland Global Rail Enterprise** is a short line railroad that operates over 10 miles of industrial track in Oakland and interchanges with the UPRR.

**Yreka Western Railroad** is a short line railroad that operates 9 miles of track in Siskiyou County and interchanges with the UPRR and Central Oregon and Pacific Railroad (CORP) in Montague.

## Rail Crossings and Engineering Branch - RCEB


---

In July 2022, the Rail Crossings and Engineering Branch (RCEB) completed the following:

|  | <b>July<br/>Closed</b> | <b>Closed<br/>YTD</b> |
|--|------------------------|-----------------------|
| <b>Crossing Incident Reviews</b>   | 12                     | 94                    |
| <b>Safety Assessments/Quiet<br/>Zones/Reviews/Training/Operation<br/>LifeSaver Presentations</b> | 47                     | 339                   |
| <b>Proceedings, Resolutions and G.O. 88-B<br/>Reviews</b>  | 7                      | 60                    |


### Rail Crossing Incident Investigations

In July 2022, RCEB closed 12 incidents at highway-rail at-grade crossings (crossings). These 12 incidents resulted in one injury and six fatalities.

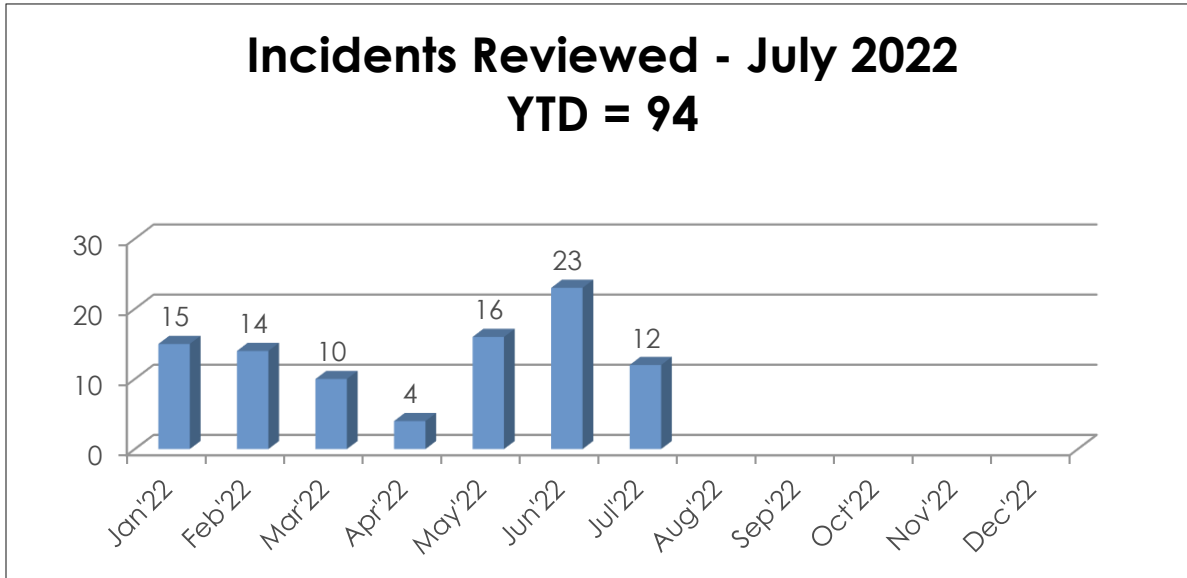

*Safety Assessments, Quiet ZONES, and Reviews*


In July 2022, RCEB completed 47 rail-crossing safety assessments involving: communications, field inspections, meetings, quiet zone reviews, staff training, diagnostic reviews, and Operation LifeSaver presentations. These activities review existing crossings and proposed changes to crossing warning devices.

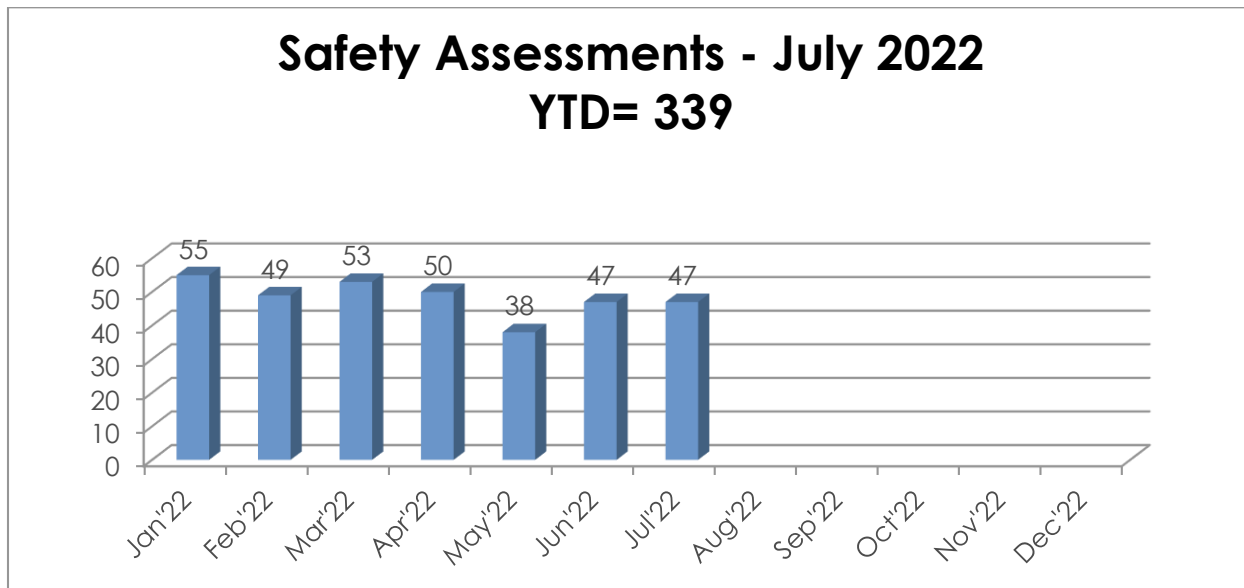

**Proceedings, Resolutions and G.O. 88B Reviews**

In July 2022, RCEB approved four General Order 88-B requests for authority for alteration to existing crossings. Also, the Commission approved two Proceedings and one Resolution.

1. PROC-A2108006 - Decision 22-07-013 - granting San Francisco Bay Area Rapid Transit District an order authorization to construct one new grade separated crossing for the Irvington Station project for pedestrian access to the Irvington Bart Station in the City of Fremont.
2. PROC-A2108020 - Decision 22-07-005 - granting Los Angeles County Metropolitan Transportation Authority East San Fernando Valley Light Rail Transit Project for an order authorizing construction of two light rail tracks at four grade-separated crossings at Metro Orange Line Bus Overpass, Metrolink Ventura County Overpass, Cabrito Road Overpass, and Interstate-5 Freeway Overpass, in Los Angeles County.
3. RESL-TED-279 - Time extension request granted for construction of a grade-separated high-speed rail crossing at Raymond Road in an unincorporated area of Madera County

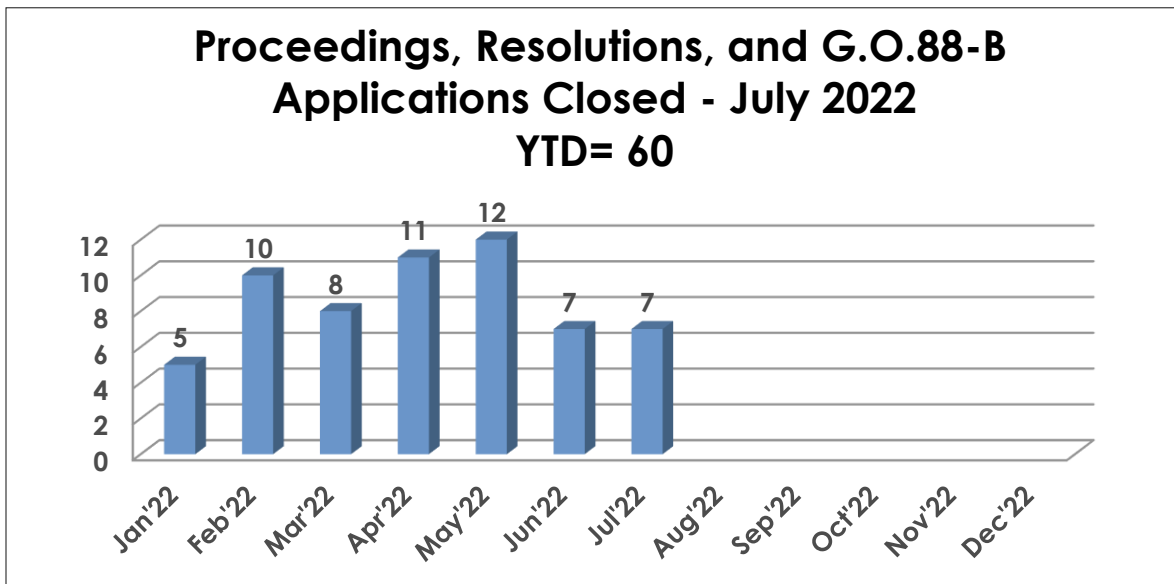

## Rail Transit Safety Branch - RTSB

---

In July 2022, the Rail Transit Safety Branch (RTSB) completed the following:

### Major Audits

---

RTSB Staff continues field work, checklist data collection, and other follow-up for the Bay Area Rapid Transit (BART) Triennial Safety and Security Review which started in late November of 2021.

RTSB Staff conducted the Santa Clara Valley Transportation Authority (SCVTA) Triennial Safety and Security Review in April 2022.

On June 6 - 17 RTSB Staff conducted the North [San Diego] County Transit District (NCTD) Triennial Safety and Security Review.

### Administrative Accomplishments

---

#### FTA Triennial Audit of CPUC's State Safety Oversight Program:

On July 11 to 19, the FTA conducted its triennial review of CPUC's State Safety Oversight program. Auditors met in person and virtually with RTSB staff, and also with representatives from various rail transit agencies.

#### Training:

RTSB staff completed the following training in the month of July:

- Nicholas Denny completed the “Effectively Managing Transit Emergencies” course offered by the U.S. Department of Transportation's Transportation Safety Institute (TSI).

#### RSSIMS Replacement Project:

The three rail branches (RCEB, ROSB, and RTSB) share a database called the Rail Safety and Security Information Management System (RSSIMS). RTSB is participating in activities to identify upgrades for the next version of the database.



## General Order and Resolution Activity

---

### Proposed Revision to GO 143-B:

RTSB management is continuing its work on drafting proposed changes to General Order 143-B “Safety Rules and Regulations Governing Light-Rail Transit.”

## RTA Ongoing Projects

---

### SAFETY CERTIFICATION AND OVERSIGHT OF RAIL TRANSIT AGENCY PROJECTS

## Bay Area Rapid Transit – BART

---

### Communications Based Train Control (CBTC):

BART entered a \$798 million contract with Hitachi Rail STS USA, Inc to design and build a modern CBTC system. The agency intends for this project to “greatly improve (its) train service.” The Project’s Safety Certification Plan (SCP) was approved by the Commission via Resolution ST-206. Contractor Hitachi executed Notice to Proceed in November 2020. Project is in preliminary design for Phase 1 – ATS upgrade at OCC.

Staff reviewed reference contract documents and did not find issues.

### BART Hayward Maintenance Complex (HMC) Project:

This project is comprised of two phases. On November 16, 2018, RTSB management approved an element of the first phase of this project, the Component Repair Shop, to commence operations. The Central Warehouse, also an element of Phase I, submitted SCVR on January 7, 2021, and RTSB management approved on January 29, 2021. Construction on the Hayward Maintenance Complex Phase II East Storage Yard began on March 1, 2019. This yard will provide a storage venue for BART revenue vehicles and provide egress to the BART A1 and A2 Mainline Tracks and the Hayward Test Track. Due to funding constraints, BART has sub-divided the HMC Phase II Project into three separate contracts, Civil Grading, Trackwork Procurement, and East Vehicle Storage Yard. At the end of the Hayward Maintenance Complex Project, BART will submit a final SSCVR that will cover both phases. HMC Phase I project scope has been scaled down and is considered by BART to be effectively complete due to budgetary constraints. BART submitted their revised SCP Rev. E detailing and amending changes to the project, which was approved by RTSB on April 13, 2022. BART has submitted their SSCVR for this phase on July 8th, 2022, and has been reviewed by Staff, and Staff has performed site verifications and inspections. Staff has found site

deficiencies await correction by BART prior to issuance of SCVR approval letter. HMC Phase II has the East Vehicle Storage Yard re-design at 60% completion and anticipates to have 90% design by July 2022.

#### Traction Power System Improvements Project (TPSIP):

Five sites have been identified for installation of new traction power substations to support the traction power system improvements portion of the Transbay Core Capacity Program. The two West Bay sites are Civic Center Station and Montgomery Street Station and have estimated completion dates by 2022. The three East Bay sites are in Oakland at Thirty Fourth Street, Concord at David Avenue and Minert Road and Richmond at Yard East, with completion dates not yet estimated. An SCP was approved via Commission Resolution (ST-239) on July 16, 2020. Civic Center and Montgomery Street stations are under construction. East Bay sites design conformance checklists are completed.

Project is reviewing issue-for-bid package for East Bay.

#### Irvington Station (IRV) Project:

The Irvington Station Project includes construction of a new station halfway between the existing Fremont and Warm Springs/South Fremont stations. The estimated completion year is 2027. The Project is in the engineering design phase. The SCP was approved under Commission Resolution (ST-240) on November 5, 2020. Project is approaching 90% design completion. SCP revision 1 was approved in May 2022.

The UPRR crossing application was approved in July by the Rail Crossing Branch.

#### New Vehicle Procurement (NVP):

BART is in the process of procuring 1,200 new rail vehicles. There are two types of new vehicles, D-Cars and E-Cars. D-Cars have an operator's cab while E-Cars do not. Upon submittal by BART, Staff reviews testing and certification documents for each group of cars prepared for service and verifies compliance with the testing and certification plan before authorizing the cars for revenue service. Due to continuing intermittent communications loss with wayside equipment and resulting system reboot, BART ceased accepting new vehicles in January 2021 until the vendor, Alstom, resolved that issue in February 2022.

A total of 359 new cars were approved as of July 2022.

## Los Angeles County Metropolitan Transportation Authority – LACMTA

---

### P3010 New Vehicle Procurement Project:

All 235 new P3010 Light Rail Vehicles (LRV) have been delivered to LACMTA from Kinkisharyo International, the vehicle manufacturer. These vehicles are intended to expand passenger capacity for the recently completed projects (Expo Phase 2 and Foothill Extension Phase 2) and the future Crenshaw/LAX line currently under construction. The P3010s have state of the art technology and upgrades to improve the passenger experience. As cars are prepared for service, Staff will recommend official approval to RTSB management after in person review of the Car History Books (testing documentation). Overall, 40 LRVs remain to be accepted by LACMTA and approved by RTSB management. To date, RTSB management has certified for revenue service 195 vehicles. In November 2021, LACMTA started to send conditional approval documentation to RTSB for vehicles with a new communication system that addressed previously identified issues. The cars that were accepted prior will have to be retrofitted to be compatible with the new communication system.

In-July 2022, Staff conditionally approved 5 vehicles for revenue service, final approval is pending Vehicle Car History Book review.

### HR4000 Heavy Rail Vehicle Procurement:

LACMTA is in the process of procuring a base order of 64, with options for up to 282 new heavy rail vehicles (HRV) to provide for the future expansions of Regional Connector and D (formerly Purple) Line Extensions, and to replace the aging HRV fleet operating on the B (formerly Red) Line subway. Resolution ST-185 approved the procurement option. The vehicle manufacturer is China Railway Rolling Stock Corporation (CRRC). These vehicles will operate as married pairs in the LA Metro red and purple (D) line subways, and trains may be made up of several married pairs of HR 4000 vehicles. The first set of married pair vehicles will be delivered to LACMTA for testing and evaluation in August of 2022 instead of June of 2022. The delay is due to the pandemic impacting progress at both the Springfield assembly site and the Changchun, China manufacturing site.

No Updates.

### Regional Connector Project:

The Regional Connector Transit Corridor (RCTC) Project is a below-grade, 1.9-mile, dual-track light rail system that will extend the existing A Line (formerly Blue Line) from the 7th/Metro Station to the existing L Line (formerly Gold Line) in the Little Tokyo area of Los Angeles. The new RCTC link will allow

passengers to travel from Azusa to Long Beach and from East Los Angeles to Santa Monica without transferring lines. The RCTC will contain three new subway stations. The contractor, Regional Connector Constructor (RCC) intends to turn over different system elements at different times to Metro once they are ready, instead of turning over everything at once. The goal is to optimize scheduling. The guideway has been turned over to Metro the weekend of June 25-26, which means that guideway access will be handled through Metro Track Allocation process instead of through the contractor.

Emergency drills (aka Full-Scale Exercises) anticipated to start in late August 2022, have been delayed. New schedule will be sent out once Project Team finalized resources to conduct the drills.

### D Line (Westside) Extension Project:

LACMTA is extending the D (formerly Purple) Line from the current terminus at Wilshire/Western station for nine miles to Westwood Veteran’s Administration Hospital. This extension will consist of approximately 9 miles of heavy rail subway with seven new stations and is separated into 3 different projects/segments, PLE1, PLE2, PLE 3. The project is funded mostly by Measure R, Measure M and federal grants. Section 1 is forecast to open in 2024, Section 2 in 2025 and Section 3 in 2027. Travel time between Westwood and downtown L.A. is expected to take about 25 minutes. The design build contractor for Segment 1 is STS (a joint venture of Skanska, Traylor, Shea). The design build contractor for Segment 2 is TPOG (a joint venture of Tutor Perini and O&G). Tutor Perini is also the design build contractor for Segment 3 tunneling and stations.

As of August 2022, Safety related design conformance verification by the Safety Certification Review Team is nearly completed for Section 1 and 2. Track and structures items remain for Section 1 and for Section 2 the documents are in the LACMTA approvals process.

### MGLFECA Foothill Extension Phase 2B:

LACMTA is extending the L (formerly Gold) Line from the current terminus of Azusa Station to the City of Montclair. The Metro Gold Line Foothill Extension Construction Authority (MGLFECA) is an independent transportation planning, design and construction agency created in 1998 by the California State legislature to resume design, contracting, and construction of the Los Angeles to Pasadena Metro Gold Line. The initial 13.7-mile, Los Angeles to Pasadena Metro Gold Line was completed and opened in 2003. Phase 2A of the Foothill Extension project was completed in March 2016 and extended the Gold Line from Pasadena to Azusa. Once construction of Phase 2B is complete, the MGLFECA will transfer the project to LACMTA to operate. In August 2019, the MGLFECA awarded the design build contract to the Kiewitt Parsons Joint Venture. Due to funding issues, the current terminus of the new alignment was changed to Pomona Station with a contract option to build to Montclair if the MGLFECA can secure additional funding. The estimated completion of the Pomona segment is early 2026. The contract option portion

from Pomona to Montclair would be on a shared corridor with Metrolink. Major construction commenced July 2020, beginning with track and warning equipment installation at the at-grade rail crossings.

As of August 2022, Safety related design conformance verification by the Safety Certification Review Team is nearly completed.

### Crenshaw/LAX Corridor Project:

LACMTA is constructing a new Light Rail Transit (LRT) line through the Crenshaw/LAX Corridor. The Line will travel 8.5 miles from the existing Metro Exposition Line at Crenshaw and Exposition Boulevards to the Green Line and will serve the cities of Los Angeles, Inglewood, El Segundo, and portions of unincorporated Los Angeles County. The project consists of Segments A, B1, B2, and C. Substantial completion of Segments A-B occurred on March 12, 2021. Now the AMC (Airport Metro Connector) Station is under construction in Segment A; it will connect to the future LAX APM. To avoid the construction zone but allow revenue service, there are preparations underway for a turnback operation north of the AMC Station. Substantial completion of Segment C occurred in June 2022. Now that the entire alignment is substantially completed, pre-revenue operations are anticipated to start no later than August 1, 2022.

Staff observed various grade crossing verification tests on 7/13, 7/18, and 7/27. Several open issues on the project have been resolved. Staff continues to work closely with LACMTA, COI and LADOT to ensure project is ready for certification.

### New A Line Project:

In the 2019 as part of the New Blue Improvements Project, LACMTA made improvements to its A Line (formerly Blue Line) that runs from Downtown Los Angeles to Long Beach. The Blue Line was renamed the “A Line” prior to fully reopening to the public on November 2, 2019. There were improvements to train control, track, overhead power, Willowbrook/Rosa Parks Station, and general station areas.

At Willowbrook/Rosa Parks Station, LACMTA would like to convert the northern emergency exit grade crossing to a public crossing. On 5/16/22 there was a virtual meeting between LACMTA and CPUC Staff to discuss this proposal and a field diagnostic meeting is scheduled for 7/12/22. Testing for the yard control upgrades is anticipated to start the weekend of 7/16/22-7/15/22 and continue into August 2022. Test results for yard control upgrades are currently going through quality control before LACMTA releases the final report. However, testing will not be complete until the discrepancies noticed during testing are resolved. They are anticipating to conduct testing again once LACMTA approves the Contractors proposed design changes. The testing is tentatively schedule for 8/20 weekend.

### East San Fernando Valley Project:

The East San Fernando Valley project alignment will start at the City of Los Angeles Van Nuys Bus Rapid Transit Orange line station and head north for 6.7 miles through the San Fernando Valley, adding 11 new LRT stations, with 34 LRVs serving this alignment. It will be a street running system for the most part with approximately 3 miles on a shared corridor with Metrolink/Amtrak. LACMTA has contracted Gannett Fleming Inc. to develop a 30/60 percent design package. LACMTA was planning to begin the procurement process of the final design build package sometime in the middle of 2021. The final design build package procurement process was delayed due to the pandemic but is expected to take place in 2022 with groundbreaking on construction to follow soon thereafter. CPUC staff have been working with the project team and LACMTA on development and drafting of the Safety Certification Plan which was approved by the commission on December 16, 2021. Forecast Revenue Service Date is June 2028.

No Updates.

### West Santa Ana Branch Transit Corridor Project:

LACMTA is evaluating a new LRT line that will connect southeast LA County to downtown Los Angeles, serving the cities and communities of Artesia, Cerritos, Bellflower, Paramount, Downey, South Gate, Cudahy, Bell, Huntington Park, Vernon, unincorporated Florence-Graham community, and downtown Los Angeles. The West Santa Ana Branch Transit Corridor (WSAB) is a 19-mile corridor project. LACMTA staff submitted a proposed funding plan/report and is exploring Public-Private Partnerships to bridge the funding gap. The Metro Board of Directors met on January 27, 2022, to discuss the selection and approval of the project terminus and a Locally Preferred Alternative (LPA). The Metro Board approved Los Angeles Union Station as the northern terminus of the West Santa Ana Branch Transit Corridor Project. The 14.8-mile Slauson/A Line to Pioneer route was also approved as the Locally Preferred Alternative (LPA) for the project's initial segment between Artesia and Downtown Los Angeles.

No Updates.

## Los Angeles World Airports – LAWA

---

### LAWA Automatic People Mover Project:

Los Angeles World Airports (LAWA), the governing body of Los Angeles International (LAX) and Van Nuys airports, is developing a multi-billion-dollar upgrade to the ground transportation system at LAX. The 2.25-mile Automated People Mover (APM) will have six new stations, three of which will connect new rental car, airport parking and Metro facilities to the airline terminals. Those in the Central Terminal Area (CTA) will provide fast and easy connections to nine airline terminals with a pedestrian walkway system. 44 cars will be built for the APM system, with the cars starting to arrive at the LAX site in the second quarter

of 2022. Car 1 was shipped from the Alstom facility in Pittsburgh, PA on 6/2/22, and Car 2 was shipped on 6/13/22.

In the month of August, LINX (Contractor) plans to begin manually driving the APM vehicles within the confines of the Maintenance and Storage Facility (M&SF). Per 7/13 APM Operations Contingency Planning Committee Meeting, all NFPA 130 required procedures have now been developed. Coordination meeting with LACMTA are scheduled to start again, the first meeting was scheduled for 7/28.

## Orange County Transportation Authority – OCTA

---

### OC Streetcar Project:

The OC Streetcar (OCSC) project consists of 4.15 miles of track between the Santa Ana Regional Transportation Center in the City of Santa Ana and the Harbor Boulevard/Westminster Avenue intersection in the City of Garden Grove. The project includes 10 stations along the alignment and the procurement of 8 Siemens S700 LRVs. The project is currently under construction. On March 4, 2022, Walsh Construction, the contractor on OCSC project, filed a lawsuit against OCTA alleging that the project breached the agreement governing the scope of work, citing numerous alleged failings on OCTA's part including neglecting to pay the company more for, or extending deadlines to accommodate, added work on the project. Walsh Construction is asking for at least \$50 million in damages as a result of the contract violations.

On July 11, 2022, OCTA submitted a GO 95 variance request to RTSB. The request is regarding 42 overhead contact system (OCS) poles that they are not able to meet the GO 95 minimum clearance requirement. OCTA has been working with RTSB since January 2021 to determine the clearance requirements of GO 95, feasibility of design changes to meet the requirements, and then mitigation methods for remaining conflicts. OCTA's proposed mitigations include relocation of Southern California Edison (SCE) secondary electric wires by two of the Overhead Catenary System (OCS) poles and installation of an industry-used protective sleeve of the communication wires adjacent to the remaining 40 OCS poles. OCTA has met with affected utility owners and received written concurrences on proposed mitigation method. Currently, RTSB is reviewing the variance request and working on a draft resolution for Commission approval.

## Sacramento Regional Transit District – SRTD

---

### LRV (Light Rail Vehicle) Procurement Project:

SRTD will be acquiring 36 new Siemens low floor light rail vehicles. SRTD acquired \$172 M for them and to make changes to its stations to accommodate the new low floor P20 Siemens S700 LRVs. Estimated in-

service date of first vehicle is projected for 11/2022. Safety Certification Plan is in development and plans and specifications have been submitted.

#### Dos Rios Light Rail Station Project:

SRTD will be completing final design and requesting bids for construction of a new light rail station. SRTD has acquired funding for the project. Estimated in-service date of the station is projected for 7/2024. Safety Certification Plan is in development and plans and specifications have been submitted.

#### Gold Line Double Track Project:

SRTD will be completing final design and requesting bids for construction of two passing tracks between Folsom and Sacramento, to accommodate 15-minute service. SRTD has acquired \$35 M for the project. Estimated in-service date of the track is projected for 6/2023. Safety Certification Plan is in development and plans and specifications have been submitted.

### San Diego Metropolitan Transit System – SDMTS

---

#### San Diego Trolley, Inc. (SDTI) SD-10 Light Rail Vehicle Procurement:

SDTI is procuring 45 LRVs known as SD10 (Car Nos. 5046 to 5091) to replace the current SD-100 models cars which will be retired from revenue service. The procurement process began September 2020 with an expected schedule completion and acceptance of all 45 LRVs by late 2023. As Siemens cars are delivered on-site at the SDTI Yard, they will undergo commissioning and dynamics tests. Staff will participate in the acceptance testing throughout the procurement process.

Staff granted permission in July for two additional SD10's to enter revenue service. To date, 14 out of 44 cars are in revenue service operation.

### Santa Clara Valley Transportation Authority – SCVTA

---

#### BART Silicon Valley (BSV) Phase II:

This BSVII is an approximately 6-mile extension of the BART system from the Berryessa/North San Jose Station through downtown San Jose in an approximately 5-mile long single-bore tunnel terminating in Santa Clara near the Santa Clara Caltrain Station. The Phase II project includes three stations in the City of San Jose (Alum Rock/28th, Downtown San Jose and Diridon Stations), one station in the City of Santa Clara (Santa Clara Station), and the Newhall Maintenance Facility. The project Safety and Security Certification Plan (SSCP) was originally Commission approved under resolution ST-83 on February 15, 2007, for the entire 16 miles extension but SCVTA Board divided the project into two phases. The BART's Silicon



Valley Berryessa extension (phase I) was placed in revenue service on June 13, 2020. On June 16, 2021, Staff received the project SCP for the phase II, and CPUC approval was sent on August 17, 2021, approving the SCP. This project is under preliminary design phase and Staff continues to attend the FTA Project Management Oversight Contractor (PMOC) meetings, Safety and Security Review Committee (SSRC) meetings, Fire Life Safety and Security Committee (FLSSC) meetings. Revenue Service Date is scheduled to be 3/31/2031.

Contract Package 1 (CP1) Systems – RFP Draft C released on 4/15/2022. The final RFP is anticipated to be issued in 4th quarter of 2022.

Contract Package 2 (CP2) Tunnel & Trackwork – Contract has been executed on 6/9/2022. Limited Notice To Proceed (LNTP) issued on 6/9/2022.

Contract Package 3 (CP3) Newhall Yard and Santa Clara Station – RFP Revision B (pre-final/draft) released 5/20/2022. RFP Revision 0 (final) release date 9/30/2022.

Contract Package 4 (CP4) Stations – Reissue RFQ tentative date January 2023. Issue RFP Revision 0 tentative date August 2023. Development of technical documents continue in support of other Contract Packages.

#### Eastridge to BART Regional Connector:

The Eastridge to BART Regional Connector (EBRC) will add 2.4 miles of double track light rail along Capitol Expressway in San Jose. This segment extends the SCVTA light rail system from the Alum Rock station to Eastridge Transit Center, entirely within the City of San Jose. The alignment traverses through a mixture of residential, commercial, industrial, and undeveloped areas. The proposed light rail alignment consists of an elevated guideway to the side and in the median of Capitol Expressway on retained earth and structure. There are no new at-grade automobile crossings, but there will be two pedestrian at-grade crossings at Eastridge Station. Resolution ST-88 dated May 24, 2007, grants SCVTA's request for approval of its Capitol Expressway Light Rail Safety and Security Certification Plan (SSCP) dated March 2, 2007. SCVTA recently submitted an updated SSCP dated January 31, 2020. Staff reviewed and approved the SSCP on July 10, 2020. The project has almost completed preliminary engineering design phase and Utility relocation is occurring currently. Staff awaits to attend future meetings related to this project.

No Updates.

#### Light Rail Signal Priority Detection Upgrades Project:

The work involved is a replacement of the Train-to-Wayside hard-wired system with a new GPS-based LRV detection system to act as primary detection system for requesting transit service priority (TSP) at non-gated signalized intersections. The necessary equipment for the work would be installed on 98 of VTA's light rail

vehicles and would be installed at 89 signalized intersections. SCVTA submitted the project SCP on May 5, 2021. Staff reviewed and approved the project SCP on June 30, 2021. At its August 19, 2021, meeting the Commission approved Resolution ST-245.

At the July 2022 Rail Activation Oversight Committee meeting the following update was provided. TSP pilot testing in the city of Sunnyvale will accommodate existing SCADA vehicle tracking circuit, via an isolated circuit by utilizing 242 isolator cards and relocating pin landings. Light Rail Vehicle Equipment Installations have begun.

## San Francisco Municipal Transportation Agency – SFMTA

---

### Central Subway Project (CSP):

SFMTA is excavating 1.7 miles of tunnel to extend the Muni Metro Third St. Line to provide a direct transit link between the Bayshore and Mission Bay areas to SoMa, downtown San Francisco, and Chinatown.

SFMTA intends to issue the SCVR on or about 9/1/22 before revenue service starts on or about 10/1/22. They anticipate pre-revenue to start towards the end of July 2022. Currently, they have been training operators on the alignment.

### LRV4 Procurement to Expand and Replace the Rail Fleet:

SFMTA LRV4 project is to procure 264 state-of-the-art Siemens LRVs. CPUC granted SFMTA approval for revenue service in 2017. After delivery of 68 cars by 2019, SFMTA found issues with the doors. SFMTA have since stopped accepting new cars, and asked Siemens to resolve the issue. Siemens redesigned sensitive edges and rubber elements for the doors for improved sensitivity for patron use and updated the rear viewing technology.

On 7/19/2022, RTSB staff sent a letter to authorize SFMTA to place two LRV4 cars (2077 & 2078) into revenue service in the near future. Currently, SFMTA has 78 LRV4's accepted and revenue service ready.

### SFMTA L Taraval Improvement Project:

In response to numerous collisions and reported safety concerns, an early implementation of measures known as the L Taraval Rapid (a non-safety certifiable) project to improve safety by adding temporary clear zones at transit stops, a transit only lane, and painted safety zones at street corners. The next step is a nearly complete rehabilitation on Taraval Street that will replace infrastructure like the worn rails, overhead wires, water, and sewer lines, as well as repave the entire street. Construction will last approximately three years. Transit service on the L Taraval will remain throughout with a combination of buses and trains. Once completed, the corridor will boast new transit priority traffic signals, bulb-outs to make pedestrian crossing

safer, new trees, high visibility crosswalks, safety boarding islands, and increased accessibility. In order to minimize disruptions during construction and maximize flexibility, the project is split in two construction segments that will overlap. During various times, there will be bus substitutions for the L Taraval so that crews can work on the rails and infrastructure beneath them. Segment A: San Francisco Zoo to Sunset Boulevard was completed in July 2021.

Segment B: Sunset Boulevard to West Portal – Construction began in early 2022 and will continue through fall 2024. L Taraval segment B construction has reached a phase where the rail tracks west of the intersection of Ulloa St and Madrone Ave have been taken offline to complete construction work. Work needs to be performed during construction to facilitate the reconstruction of the water and sewer mains as well as replace the tracks and overhead lines. OCS work will be performed sequentially along the L Taraval line from West Portal to Sunset Blvd.

From July 11 through 31, 2022, Segment B construction will focus on replacing water and sewer lines.

From August 1 through 13, 2022, work will continue on the water and sewer lines, as well as on the overhead contact system (OCS). OCS work will be performed at night and includes potholing, foundation work, and installation of new poles.

## Appendices

---

### GENERAL DEFINITIONS

#### Corrective Actions Plans

General Order 164-E defines Corrective Action Plan as a plan developed by a Rail Transit Agency that describes the actions the RTA will take to minimize, mitigate, control, correct, or eliminate risks and hazards, and the schedule for implementing those actions.

#### Accident Investigations

Per General Order 164-E, the Commission must be notified within 2 hours by rail transit agencies of accidents if they include one of the following: a fatality (occurring at the scene, or within 30 calendar days following the incident); one or more persons suffering “serious injury” (as defined in GO 164-E); a collision involving a rail transit vehicle and another rail transit vehicle, or individual; a derailment of any rail transit vehicle at any location, at any time, whatever the cause; an evacuation for life safety reasons; or a runaway train. “Courtesy notices” are not included in these statistics.

## Monthly RTSB Data

---

### Statistics Summary


Table 1. Investigation &amp; CAP Data

| <b>Investigations</b>                       | <b>July 2022</b> | <b>YTD2022</b>  |
|---|------------------|-----------------|
| <b>Accidents Reported</b>                   | 37               | 205             |
| <b>Accident Investigations Closed</b>       | 12               | 185             |
| <b>Complaints Investigated</b>              | 0                | 3               |
| <b>Rail Transit Inspections</b>             | 50               | 257             |
| <b>Triennial Review</b>                     | 0                | 3               |
| <b>Corrective Action Plans</b>              | <b>July 2022</b> | <b>YTD 2022</b> |
| <b>New Corrective Action Plans</b>          | 32               | 195             |
| <b>From Triennial Review</b>                | 0                | 0               |
| <b>From Incidents</b>                       | 6                | 47              |
| <b>From Internal Safety/Security Audits</b> | 3                | 12              |
| <b>From Rail Transit Inspections</b>        | 23               | 130             |
| <b>From Hazard Management</b>               | 0                | 6               |
| <b>Closed Corrective Action Plans</b>       | 37               | 185             |
| <b>From Triennial Review</b>                | 0                | 4               |
| <b>From Incidents</b>                       | 1                | 20              |
| <b>From Internal Safety/Security Audits</b> | 1                | 7               |
| <b>From Rail Transit Inspections</b>        | 35               | 154             |
| <b>From Hazard Management</b>               | 0                | 0               |

Data collected from RSSIMS


Ongoing Data / Trends

Table 2. Accidents by Type

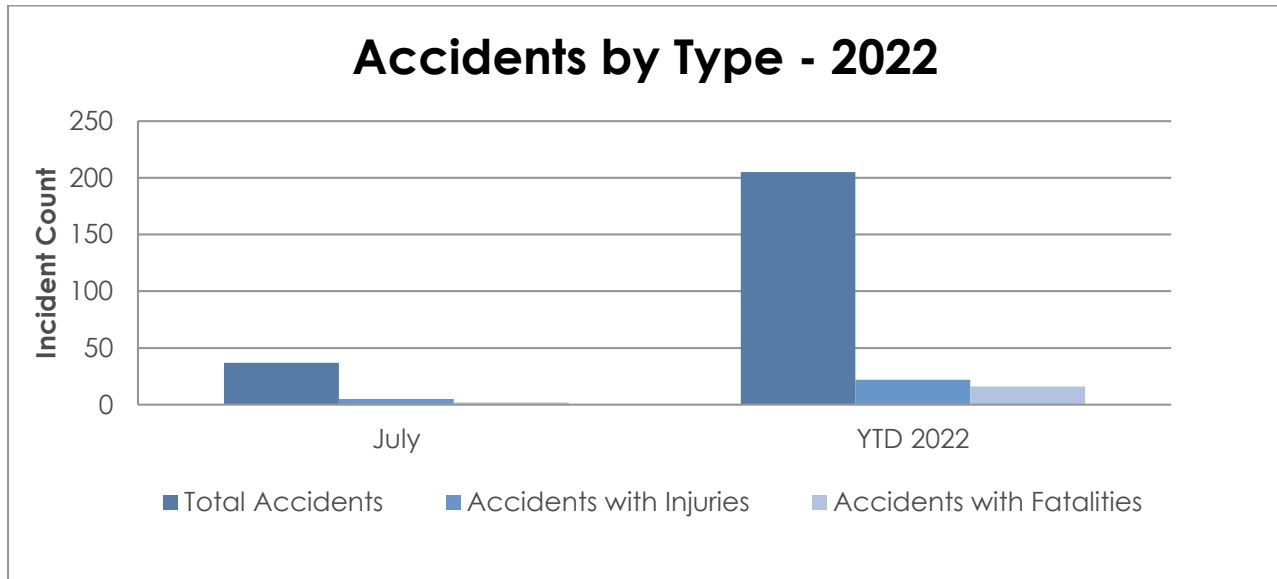


Data collected from RSSIMS

Table 3. Inspections & CAPs

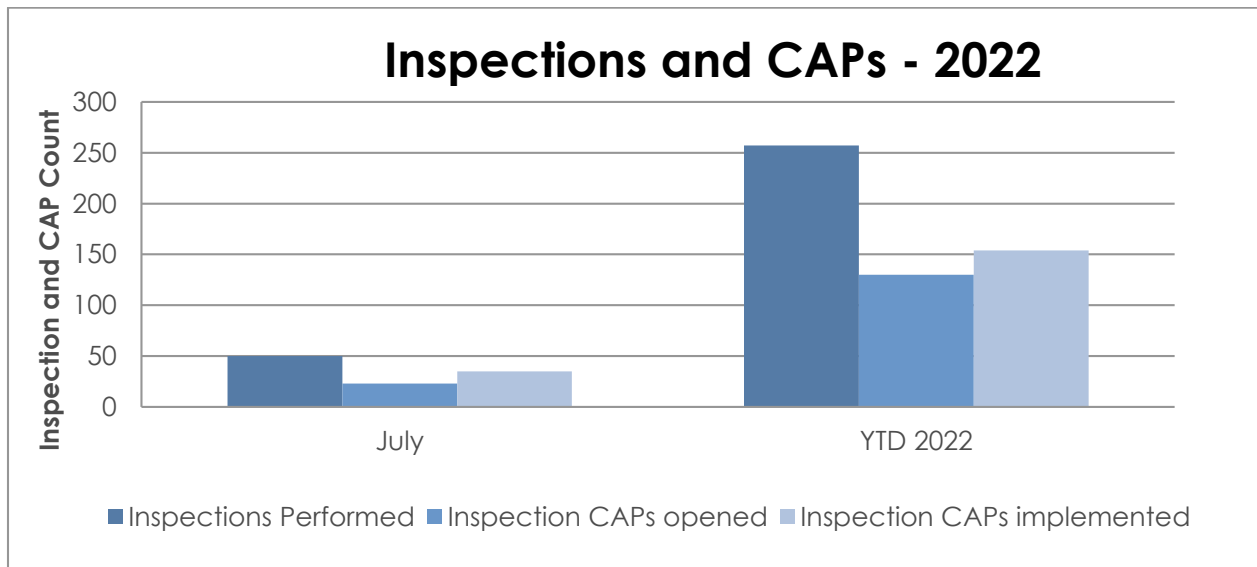


Data collected from RSSIMS

Table 4. CAPs Opened

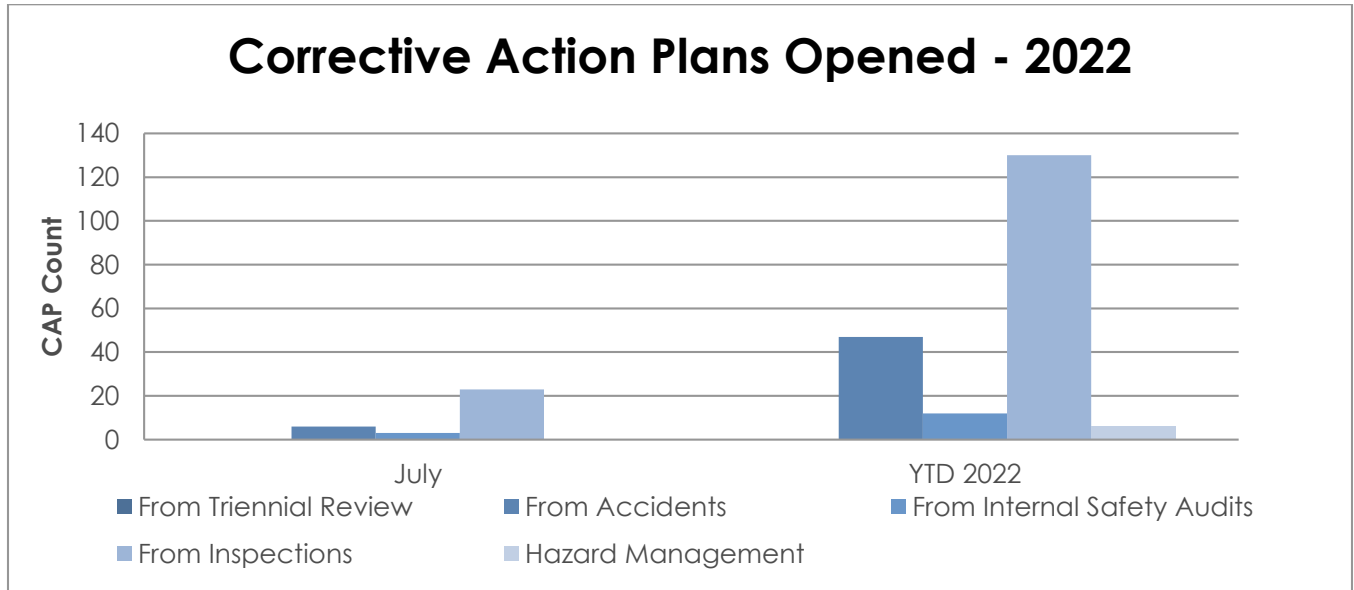

Data collected from RSSIMS

Table 5. CAPs Closed

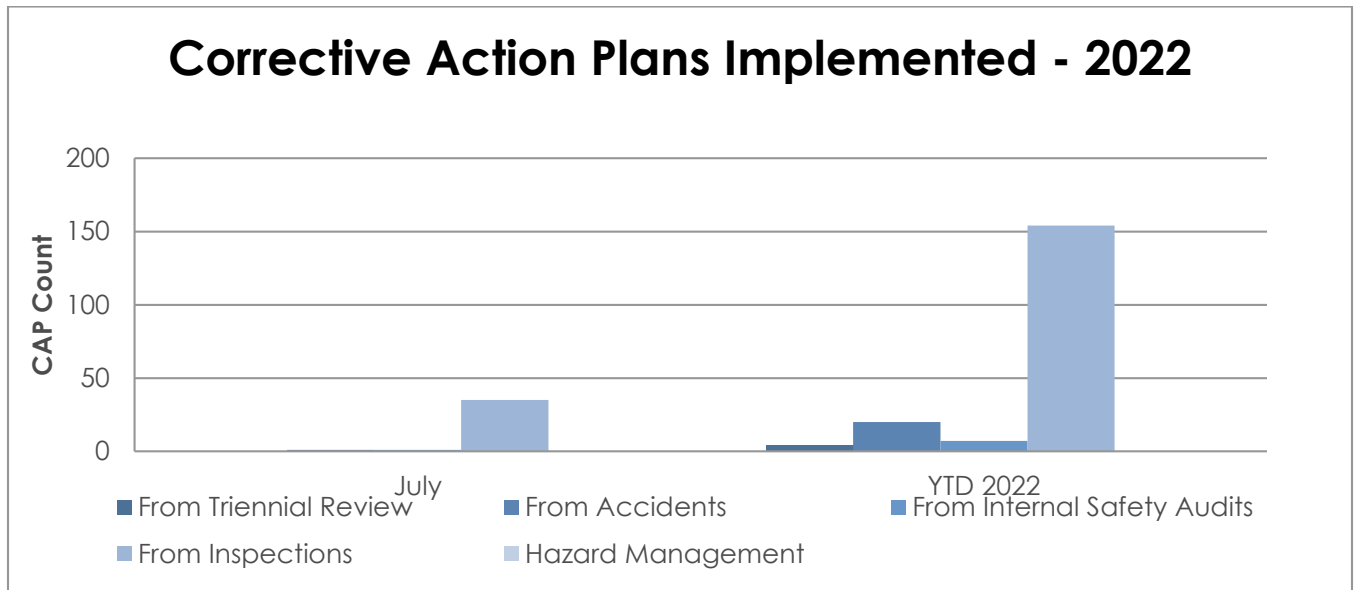

Data collected from RSSIMS
